

Tourism Diversification and Resilience in The Gambia (P177179)

Implementation Support Review and Business Ready (B-READY) Analytics

May 10, 2024

AIDE-MÉMOIRE

I. INTRODUCTION

1. A World Bank (WB) team¹ visited Banjul, The Gambia, from April 29 to May 10, 2024, to conduct implementation support activities for the Tourism Diversification and Resilience (TDR) in The Gambia Project (P177179). The mission's objectives included discussions on overall project implementation, with a specific focus on the critical path for Component 2: *Infrastructure support for the diversification and resilience of the tourism sector*, updating the implementation plan, reviewing financial management compliance, introducing the new co-Task Team Leader (co-TTL), hosting an ecotourism regional workshop, organizing a series of capacity building workshops on Business Ready (B-READY), and kickstarting the activities under the Women Entrepreneurs Finance Initiative (WeFi).

2. This Aide Mémoire summarizes the mission's findings and agreements and provides an update on the status of the TDR project's implementation. The World Bank team expresses gratitude to the Government of The Gambia, particularly the Honorable Minister of Finance and Economy (MoFEA), Minister of Tourism and Culture (MoTC), their respective Permanent Secretaries (PS), and all key stakeholders, for their leadership and support throughout the mission.

3. The mission proposes to upgrade the performance ratings for Component 1, Project Management and Procurement, from 'Moderately Unsatisfactory' to 'Moderately Satisfactory' due to significant progress in project implementation (details are presented in the sections below).

II. KEY PROJECT DATA AND RATINGS

Project Data		Project Data	USD (millions)
Approval Date	09-Jun-2022	Closing Date	30-Jun-2027
Signature Date	05-Jul-2022	Original Project Amount	\$68.00
Effectiveness Date	03-Oct-2022	Total Disbursement	\$7.42
Mid-Term Review (Planned)	02-Dec-2024	Disbursement in FY	\$2.40

Project Ratings:	March 22, 2024 ISR	This Mission
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Component 1: Policy framework and MSME participation	● Moderately Unsatisfactory	● Moderately Satisfactory
Component 2: Infrastructure support	● Moderately Satisfactory	● Moderately Satisfactory
Project Management	● Moderately Unsatisfactory	● Moderately Satisfactory
Monitoring and Evaluation	● Moderately Satisfactory	● Moderately Satisfactory
Procurement	● Moderately Unsatisfactory	● Moderately Satisfactory
Financial Management	● Satisfactory	● Satisfactory

¹ The mission consisted of Douglas Pearce (Practice Manager, EAWF1); Rafael Pardo (Senior Financial Sector Specialist and TTL); Keren Charles (Senior DRM Specialist, co-TTL, outgoing); Isabelle Kane (Senior DRM Specialist and co-TTL, incoming); Anupa A. Pant (Private Sector Specialist and co-TTL); Jose Miguel Villascusa Cerezo (Tourism Consultant); Brahim Hamed (Senior Procurement Specialist); Scott Ferguson (Senior Flood Risk Management Consultant); and Fabio Cian (DRM Consultant). Nancy Njie (Environmental Consultant) and Momodou Sey (Consultant) joined from The Gambia. Frederic Meunier (Economist); Kaliza Karurewa (Senior Private Sector Specialist) and Aji Oumie Jallow (Administrative Assistant) joined for the B-READY workshops. Louise Twining-Ward (Senior Private Sector Specialist and Tourism Technical Lead) joined a week after to host an ecotourism regional workshop and provide tourism implementation support to the PIU.

Overall ESS Performance	● Satisfactory	● Satisfactory
-------------------------	----------------	----------------

III. IMPLEMENTATION PROGRESS AND KEY FINDINGS

4. The TDR has been under implementation for nineteen months since its effective date. A Project Implementation Unit (PIU), Project Steering Committee (PSC), and two Technical Working Groups (TWG) have been established. Essential governing documents have been produced, and the Terms of Reference (ToRs) for critical activities have been finalized. Implementation pace has picked up and the project is on track towards the achievement of the PDO.

5. The WB team conducted a scenario analysis of the implementation plan to assess the risks of timely completion of the coastal works. The analysis produced both optimistic and worst-case scenarios, which helped to assess the likelihood of finishing the coastal works within the current project timeline. This timeline includes various phases: feasibility studies, pre-design and design, environmental and social impact assessments (ESIAs), and procurement processes. The WB team identified critical milestones and strategies to optimize the implementation planning for earlier coastal protection works initiation. The WB team will monitor the progress of these milestones, including an assessment of progress and status of deliverables by the engineering firm to reevaluate sub-component risks during the next supervision mission during the third quarter of 2024 (Q1 FY25).

6. The WB team also conducted a multi-stakeholder workshop focused on coastal protection and its relevance to the tourism sector. The workshop was well-received. It was also agreed that a study trip to Saly, Senegal, would be organized in the coming months to observe the WB-funded coastal protection efforts in the resort area, in coordination with the World Bank.

IV. TDR PROJECT STATUS AND DECISIONS PER COMPONENT / ACTIVITY

Component 1: Policy framework and MSME participation (US\$13 million)

Subcomponent 1a: Improved institutional capacity for data-driven planning, marketing, and branding (US\$3.875 million)

Statistics and Data for Tourism Activities (US\$1.15 million)

7. During the mission, the WB team confirmed the successful progress of the pilot training activities that occurred from April 29th to May 3rd. The outcomes of this sub-activity will inform the allocation and scope for the subsequent two activities: (ii) tourism statistical capacity building, and (iii) acquisition of equipment for tourism statistical data collection and analysis.

Development and Implementation of a Tourism Marketing Strategy for The Gambia (US\$2.025 million)

8. During the mission, technical proposals submitted by international firms were opened. Over the subsequent week, the PIU evaluation committee convened and submitted the evaluation form to the WB for No Objection. The WB team issued its No Objection on May 14th, 2024. The financial proposals were opened on May 15th. The PIU is currently preparing the final evaluation report and recommendations.

GTHI Support to address the problem of “tourism brain drain” (US\$450,000)

9. The WB team provided feedback on the Capacity Assessment. There is consensus on the report’s shortcomings and some concerns regarding the quality and technical deliverables. The team also met with the GTHI to gauge their satisfaction and involvement with the ongoing work. While they expressed high satisfaction with the collaboration on the Kitchen design, they highlighted the need for more effective engagement in curriculum development. The tourism specialist will specifically focus on providing assistance with this aspect.

Short-Term Recovery Plan (US\$250,000)

10. The short-term recovery plan includes three sub-activities: (i) training for beach workers, bird watching guides, fruit sellers, and customer service personnel; (ii) the Gambian Authorities' outreach and marketing mission to Nigeria; and (iii) the international visitor survey.

(i) The training has been successfully contracted and is expected to be completed within three months. The WB team urged the PIU to ensure a high proportion of women are trained, in line with the findings of the recent PROBLUE gender assessment shared with the PIU.

(ii) The team had a multi-stakeholder roundtable discussion to resolve differences in approach and budget for the Gambian authorities' outreach and marketing mission to Nigeria. These issues were successfully settled, the concept note, and budget were finalized, and the WB provided its No Objection.

(iii) The team confirmed the successful implementation of the International Visitor Survey (IVS) at Banjul International Airport, marking the first IVS for The Gambia. The results are highly anticipated, with the analysis expected in the week of May 25th.

Subcomponent 1b: Increase participation of tourism MSMEs within the selected destinations (US\$9 million)

Technical and compliance support to tourism MSMEs (US\$4 million)

11. The component is beginning to show progress with the hiring and onboarding of the Management Company (MC), and the finalization of the inception report, which details the sequence of activities, timelines, and deliverables for the coming year. Although some tasks from the last mission are complete, some important activities such as signing of MoUs with hotels on supplier development program are still pending. Interventions during the mission, however, have helped to address many of the challenges, and the outstanding tasks are expected to be completed within the next quarter. These tasks include setting up the MC's office and onboarding staff, finalizing the Lead Firm's needs assessment and priorities, orienting Business Development Managers (BDMs), and screening the first cohort of 50 SMEs. The WB team has stressed the need to take necessary measures to avoid further delays and to ensure the timely completion of activities as outlined in the inception report. The PIU has agreed to bi-weekly progress meetings with the MC, and the Tourism Specialist is fully briefed on the component's importance to the project, ensuring focused support.

Matching grants to support tourism value chain participation for MSMEs (US\$5 million)

12. This activity is scheduled to begin six months after the completion of capacity building by the selected MSMEs, approximately, around October 2024.

Component 2: Infrastructure support for the diversification and resilience of the tourism sector (US\$50 million)

13. After experiencing significant delays, the activities within sub-component 2a have progressed with the recruitment of the engineering firm Royal HaskoningDHV (RH) and the launching of the coastal protection infrastructure design studies. The PIU analyzed the contracts for this component and reported that out of the 14 contracts expected under this component, 8 have been signed or are in progress. These account for a commitment of US\$2.6 million, approximately 5% of the allocated budget for this component. Most of the disbursement is expected to occur once the infrastructure works commence, which is projected to happen within the next two years.

Subcomponent 2a: Protection, rehabilitation, and integrated management of coastal areas (US\$45 million)

14. The mission reviewed and updated the implementation plan, emphasizing the reduction of procurement timelines and the acceleration of activities. However, if the PIU can reach an agreement with RH, the engineering firm, to expedite the delivery, particularly for the less complex Kunta Kinteh site, civil works for this sub-component could start as early as February/March 2025 at this site. The mission also highlighted the importance of developing the environmental and social (E&S) instruments from the early stages of the preliminary design to

prevent delays in the initiation of works. The timeline for the E&S instruments has also been mapped in the revised implementation plan (Annex 1). Should the team determine that the sub-component is at risk, it will contemplate downgrading the sub-component and elevating its risk profile.

Preliminary design of coastal Beaches Fajara-SeneGambia and Kunta Kinteh Island (US\$900,000.00)

15. This activity is ongoing with the inception report expected from RH in May 2024. The activity involves conducting feasibility studies and developing pre-designs, detailed design, and bidding documents for coastal protection in the Kunta Kinteh site. Based on the current timeline, the pre-designs are expected by April 2025; However, the PIU and GAMWORKS will work with the firm to reduce this timeline to allow earlier completion design studies and commencements of civil works.

16. The inception report from RH expected for May 2024 has been shared (post-mission). The coastal protection works for the Kotu site would take longer to be completed. Because of these works' complexity, RH's contract only includes the feasibility and preliminary design studies at this stage. The complementary studies including preparation of detailed design and bidding documents would be procured later, once the preliminary design stage deliver clear data and engineering solution.

Subcomponent 2b: Integrated tourism product development and diversification of selected Tourist Development Areas (TDAs) (US\$5 million)

Demand and Destination Sites evaluation and assessment (US\$250,000)

17. The objective of this activity is to assess key tourism sites, prioritize them, and develop a costed plan for enhancement for those selected. The consultants' mission, which took place from March 6 to 25, 2024, has produced its first deliverable: the Draft Destination Long List Report was submitted on April 19. Despite a slight delay as per the Implementation Plan, its quality was high, necessitating only minor comments. The Final Destination Long List is expected by the end of May. The next steps include an in-depth Destination Assessment report defining the top 10 shortlisted sites. The final deliverable, a Destination Assessment and accompanying presentation, is scheduled for completion on July 12, 2024, and will provide the Government with a concrete investment plan for the key tourism sites, with dissemination planned by August 2, 2024.

18. There is also a need to clarify the scope of the activity in relation to the feasibility and design work underway at the Kunta Kinteh site, due to its apparent overlap. The pending issue is whether the Albreda and Juffreh areas are included in both studies and, if so, how to address any redundancy. A meeting with the Project Implementation Unit (PIU) to resolve this will be arranged by the end of May 2024.

Assessment of River Jetties (US\$295,000)

19. The objective of this activity is to evaluate the jetties along the River Gambia to identify which should be prioritized for rehabilitation or reconstruction. This will include identifying potential sites for new jetties and preparing both preliminary and detailed design studies, along with bidding documents for the civil works. The activity, which is currently under contract is set to begin with an inception mission from RH firm in May 2024. The mission recommended that the timeline for these studies could be reduced, and the works could possibly be combined under the same contract as the coastal protection efforts on Kunta Kinteh Island, which include the rehabilitation or reconstruction of its two jetties.

GTHI Kitchen Expansion Design and Supervision (US\$35,000)

20. The activity, which is contracted and ongoing, has been met with a high level of satisfaction from GTHI. However, there have been delays in receiving feedback, which GTHI has committed to addressing in the future. The consultant has completed the designs and, following a review by GAMWORKS, revisions are made to integrate GTHI's feedback. The final designs are now expected by June 2024. After this, the procurement process for the necessary works and goods will be initiated. During a field visit, GTHI indicated the need for new parts for the

laundry training machines located adjacent to the new kitchen and requested support for this. Additionally, a historic tree located in the GTHI parking area requires additional protection measures prior to the start of work, which requires consultation with environmental standards experts. The works are expected to start by July 2024.

Gender Assessment of the Tourism Sector in The Gambia (US\$28,000):

21. The ongoing assessment aims to expand upon the findings of the recent gender assessment conducted under the PROBLUE trust fund. It will identify and document existing gender disparities and significant gender-related challenges at the sites identified for upgrading.

Component 3: Project management, monitoring and evaluation (US\$5 million)

Procurement:

22. The PIU has consistently updated the procurement plan using the Systematic Tracking of Exchanges in Procurement (STEP) tool. STEP analysis indicates that out of nineteen recorded procurement activities, thirteen are for consulting services, five for goods, and one for non-consulting services. The Project Procurement Strategy for Development (PPSD), approved by the Bank, is accessible on STEP, with all relevant notices published accordingly.

23. In terms of contract implementation, the mission noted that twelve activities have signed contracts within the system, including those for the MC, GAMWORKS, and the feasibility studies, while seven activities are facing delays in the procurement process.

24. The mission acknowledged the improved use of STEP since their last visit. Nonetheless, they recommend further enhancements in the system's data accuracy, completeness, and timeliness, especially regarding contract administration, including payment, delivery, and completion details.

25. To accelerate implementation of Component 2 and works contracts, the PIU should: (a) expedite the feasibility studies to finalize design and technical specifications promptly, (b) improve the procurement process and ensure swift evaluation of bids and proposals in collaboration with the procurement committee, (c) keep STEP information current and precise, and (d) ensure close collaboration between PIU staff and project stakeholders, as stipulated in the project implementation manual.

Monitoring and Evaluation (M&E):

26. A follow up meeting will be held with the M&E expert to review the MEMIS system for capturing M&E results.

Project Implementation Unit / Tourism Specialist:

27. The PIU's Tourism Specialist joined the mission. The team facilitated an introductory meeting between the new Permanent Secretary (PS) and the GT Board to acquaint them with the specialist. The PS has promptly involved the specialist in updating the tourism policy and in formulating an action plan and budget for its implementation. The specialist will closely monitor activities that are experiencing difficulties or delays, as well as those requiring expertise not readily available within the PIU, such as curriculum development, MSME support, and marketing.

V. OTHER ACTIVITIES CARRIED OUT DURING THE MISSION

28. **Business READY:** From April 22nd – 25th, 2024, the WB team, in coordination with the Ministry of Trade, Industry, Regional Integration and Employment (MoTIE), organized a series of thematic workshops on each of the new B-READY topics and initiated the reorganization of the reform delivery on 10 B-READY topics. The workshop also provided an outcome of the recent Enterprise Survey Findings and the Gambia Economic Update. The Gambia is among the first 51 economies measured in the B-READY report that will be published on September 25, 2024. For the first report, the Government of the Gambia was not aware of the processes and mechanisms used in the B-READY assessment. The World Bank team emphasized the need to be better prepared for the second report

that will start in September 2024, particularly in appointing focal points for each technical working group responsible for responding to the questionnaires on behalf of the Gambian Government. The workshop identified some potential quick wins particularly around Transparency. The Gambia currently does not publish most of the regulatory information measured by B-READY. The team had a debriefing meeting with Honorable Baboucarr Ousmaila Joof, Minister of Trade, Industry, Regional Integration & Employment and emphasized the need to secure high level political commitment to mobilize participation of wider group of participants. The Ministry has requested for a follow up technical assistance to support working groups on reviewing and responding to the questionnaires and identification of areas of improvement in preparation for a reform action plan.

29. Field visit to Kunta Kinteh Island: The WB team visited Kunta Kinteh Island as part of a field visit to review areas of future intervention of the project. The WB team also visited sections of the West Coast beaches, which are also an area of future intervention under Component 2a.

30. Women Entrepreneurs Finance Initiative (WeFi Sahel-The Gambia): The WB team is leveraging the WeFi funding to enhance the linkages agenda, specifically by promoting sourcing partnerships between women-led cooperatives and tourism lead-firms. The consultants have been recruited and are in the process of screening 20 core groups of women led rural enterprises in collaboration with the Gambia Inclusive and Resilient Agricultural Value Chain Development Project (GIRAV). For the next 10 months, the project will adopt IFC's Agribusiness Leadership Program (ALP) to provide coaching to women owned cooperatives, on key performance areas such as financial management, market, leadership skills and diversity.

31. West Africa Ecotourism Network (WAEN) Workshop: The WAEN event took place at Bakadaji Hotel in Serrakunda on May 6th and 7th, inaugurated by the Honorable Abdoulie Jobe, MoTC. A total of 278 individuals registered for the event online, with over 50 attendees from across the region participating in person, including representatives from the GT Board, Hotel Association, ecotourism operators, and tourism and development students from The Gambia, among others. The event featured eight one-hour Masterclasses on various ecotourism-related topics such as ecolodge design, coastal resilience, ecotour design, customer communication, and community-based tourism. These sessions were recorded and will be made available on the WAEN website. Participants were highly engaged and expressed satisfaction with both the organization of the event and the quality of the presentations. The event received support from PROBLUE, PPIAF, and the WACA project.


VI. NEXT STEPS AND AGREED ACTIONS

32. The next Implementation Support Mission, set for early Q3 2024 (Q1 FY25), will assess progress on agreed actions, with a focus on the RH firm's feasibility studies.

	Actions	Due Date
1	Complete the Gambian Authorities' outreach and marketing mission to Nigeria	May 2024
2	Agree on budget for tourism IT and data equipment	May 2024
3	Start the short-term training with a focus on recruiting women participants	June 2024
4	Setting up the MC's office and onboarding staff	June 2024
5	Finalizing the Lead Firm's needs assessment and priorities	June 2024
6	Orienting Business Development Managers (BDMs)	June 2024
7	Screening the first cohort of 50 SMEs.	July 2024
8	Complete the quality review of the inception report for the coastal protection design study and get a final version from the firm including clear agreed steps and timeline	June 2024
9	Complete contracting of Marketing Firm	July 2024
10	Plan and undertake Senegal coastal protection field trip	Q3 2024
11	Finalize the recruitment of a coastal engineer technical assistant to support the PIU on coastal protection activities and supervision	September 2024

ANNEXES

Annex 1: Implementation plan for Component 2 revised based on lessons learned.

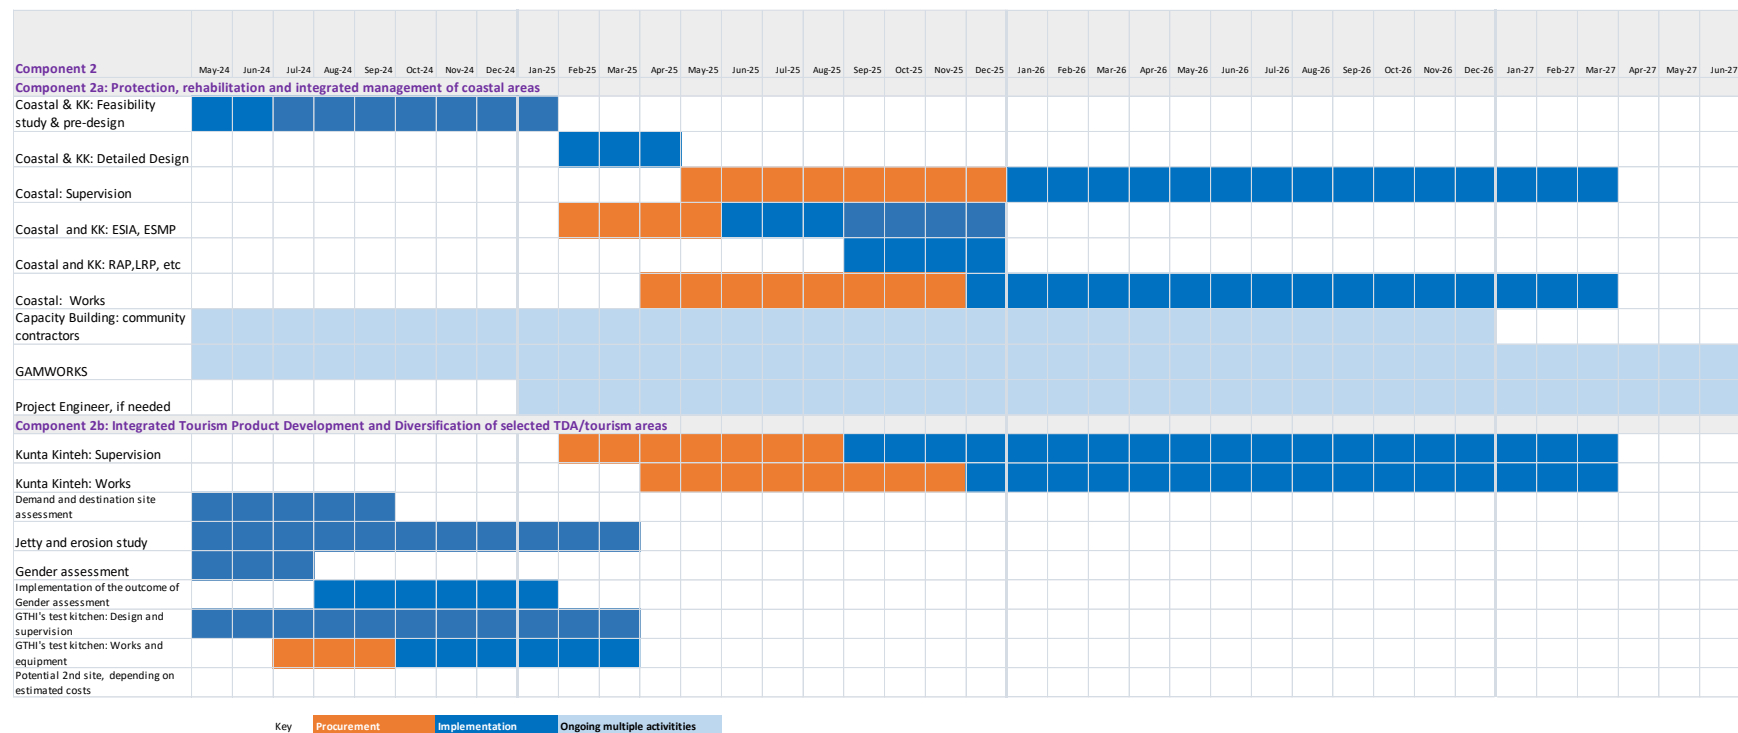

Key Milestones for Civil Works (Coastal and Kunta Kinteh)	
	End of
Coastal Works & Kunta Kinteh Island Feasibility Studies and Pre-Design:	Jan-25
Coastal Works & Kunta Kinteh Island Detailed Design:	Apr-25
Coastal Civil Works Procurement:	Dec-25
Coastal Civil Works Supervision:	Mar-27
Coastal Works ESIA, ESMP Procurement:	May-25
Coastal Works ESIA, ESMP Assessments:	Dec-25
Coastal Works & Kunta Kinteh Island RAP, LRP:	Dec-25
Kunta Kinteh Island Works Procurement:	Sep-25
Kunta Kinteh Island Works Supervision:	Oct-26

Annex 2: Status of Agreements from the previous AM

	Actions	Due Date	Responsible	Status Update
1	Inception Report by the Management Company	Feb 29, 2024	MC	Complete. Inception report was received 28 th February 2024.
2	Agree with stakeholders and recruit the identified Tourism Specialist	Mar 8, 2024	PIU/MoTC/GTB	Complete. Contract signed 22 nd March 2024
3	Award and sign the contract of the Gender Assessment	Mar 8, 2024	PIU	Complete May 7 th and under implementation.
4	Finalize agreement for Visitor Survey	Mar 8, 2024	PIU/Contractor	Complete. Addendum Contract signed 28 th February 2024, and activity is on course.
5	Finalize ToRs for capacity building of tourism workers and launch REoI	Mar 8, 2024	PIU	Complete. REoI launched 15 th March 2024
6	MoU with Hotels on Supply Development	Mar 22, 2024	MC	Not complete. Management Company at Inception Report finalization stage.
7	Inception report for the engineering consultant for studies and pre-design	Mar 25, 2024	Consultant	Complete After the Mission: Inception Report received on May 23
8	Finalize the recruitment of the procurement assistant	Mar 29, 2024	PIU	Complete. Contract signed 14 th March 2024.
9	Finalize the procurement process of the firm to conduct the Marketing Strategy	Mar 29, 2024	PIU	Ongoing and near completion- Standstill period expires on the 31st May 2024.
10	Complete Nigeria Study Tour	Apr 30, 2024	PIU	Ongoing (May 20 th -30 th 2024)
11	Complete Human Resource Capacity Building (Short Term Recovery)	Apr 30, 2024	PIU	On-going and near completion—negotiation completed and awaiting Contract Signature.

Annex 3: Mission Schedule

Mission Day 1: Monday, April 29, 2024	
Project Implementation Unit	Meeting of MoTC, PIU, GTB, NCAC, GTHI on review of outstanding issues in Aide Memoire
Project Implementation Unit	Meeting with PIU on General Project Status and Introduce Isabelle Kane
Project Implementation Unit	Detailed Meeting on Activities under Component 2 - Critical Path
Mission Day 2: Tuesday, April 30, 2024	
Project Implementation Unit	Coastal Resilience presentation from WB team
Royal HaskoningDHV / Cityscapes	Feasibility Studies Meeting with RH
Ministry of Tourism and Culture	Courtesy Meeting with Hon Minister, PS and DPS to brief on Mission Objectives
Project Disbursements & Procurement	Detailed Meeting on Financial Management, Disbursements & Procurement
Mission Day 3: Wednesday, May 1, 2024	
Visit to Kunta Kinteh Island	Field Visit to Kunta Kinteh Island and Albreda
Mission Day 4: Thursday, May 2, 2024	
PIU, GTB, NCAC, GTHI, MECCNAR, MOFEA, NEA, WB team, MoTC,	Meeting with stakeholders on coastal resilience & Presentation on Senegal case study (TBC)
Project Implementation Unit	Discussion on component 1 & Management Company
Wrap up with PIU	Mission conclusions & Next steps
WB/CMU	Bank team meet with CMU
Mission Day 5: Friday, May 3, 2024	
Debriefing with MoTC	Mission conclusions & Next steps
Mission Week 2: May 6-7, 2024	
WAEN Workshop	
Mission Week 2: Monday, May 8-10, 2024	
Project Implementation Unit and Tourism Stakeholders	Implementation Support for Component 1

Annex 1: List of officials met

Name	Title	Institution
Hon. Abdoulie Jobe	Minister	Ministry of Tourism and Culture (MoTC)
Cordu L. Jabang-Senghore	Permanent Secretary	Ministry of Tourism and Culture (MoTC)
Isatou Drammeh	Deputy Permanent Secretary	Ministry of Tourism and Culture (MoTC)
Hon. Rohey John-Manjang	Minister	Ministry of Environment, Climate Change and Natural Resources (MECCNAR)
Mamadi Dampha	Deputy Permanent Secretary	Ministry of Finance and Economic Affairs (MoFEA)
Momodou Lamin Singhateh	Director General	Gambia Tourism and Hospitality Institute (GTHI)
Sheriff Conteh	Deputy Director General	Gambia Tourism and Hospitality Institute (GTHI)
Abubacarr S. Camara	Director General	Gambia Tourism Board
Musa Dem	Manager	Gambia Tourism Board
Hassoum Ceessay	Director General	National Center for Arts and Culture (NCAC)
Mam Marie Njie		National Environment Agency (NEA)
Elizabeth Carayol-Ndong	Technical Director	Gambia Agency for the Management of Public Works (GAMWORKS)
Momodou BT Senghore	Senior Project Manager	Gambia Agency for the Management of Public Works (GAMWORKS)
Momodou Ceessay	Project Director	TDR Project Implementation Unit
Brian T. Mullis	Tourism Specialist	TDR Project Implementation Unit
Musa D Kora	Financial Management Specialist	TDR Project Implementation Unit
Bakary E Kujabi	Procurement Specialist	TDR Project Implementation Unit
James B Mendy	Monitoring & Evaluation Specialist	TDR Project Implementation Unit
Fanta Jatta-Sowe	Gender-Based Violence Specialist	TDR Project Implementation Unit
Salimatou Taal	Social Risk Management Specialist	TDR Project Implementation Unit
Rohey Samba-Jallow	Communication & Stakeholder Engagement Specialist	TDR Project Implementation Unit
Foday Fatty	Environmental Risk Management Specialist	TDR Project Implementation Unit
Ebrima Jatta	Accountant	TDR Project Implementation Unit
Alagie Laye	Administrative Assistant Technical	TDR Project Implementation Unit
Yahya Jobe	Administrative Assistant Operations	TDR Project Implementation Unit
Kodou Jagne	Procurement Assistant	TDR Project Implementation Unit
